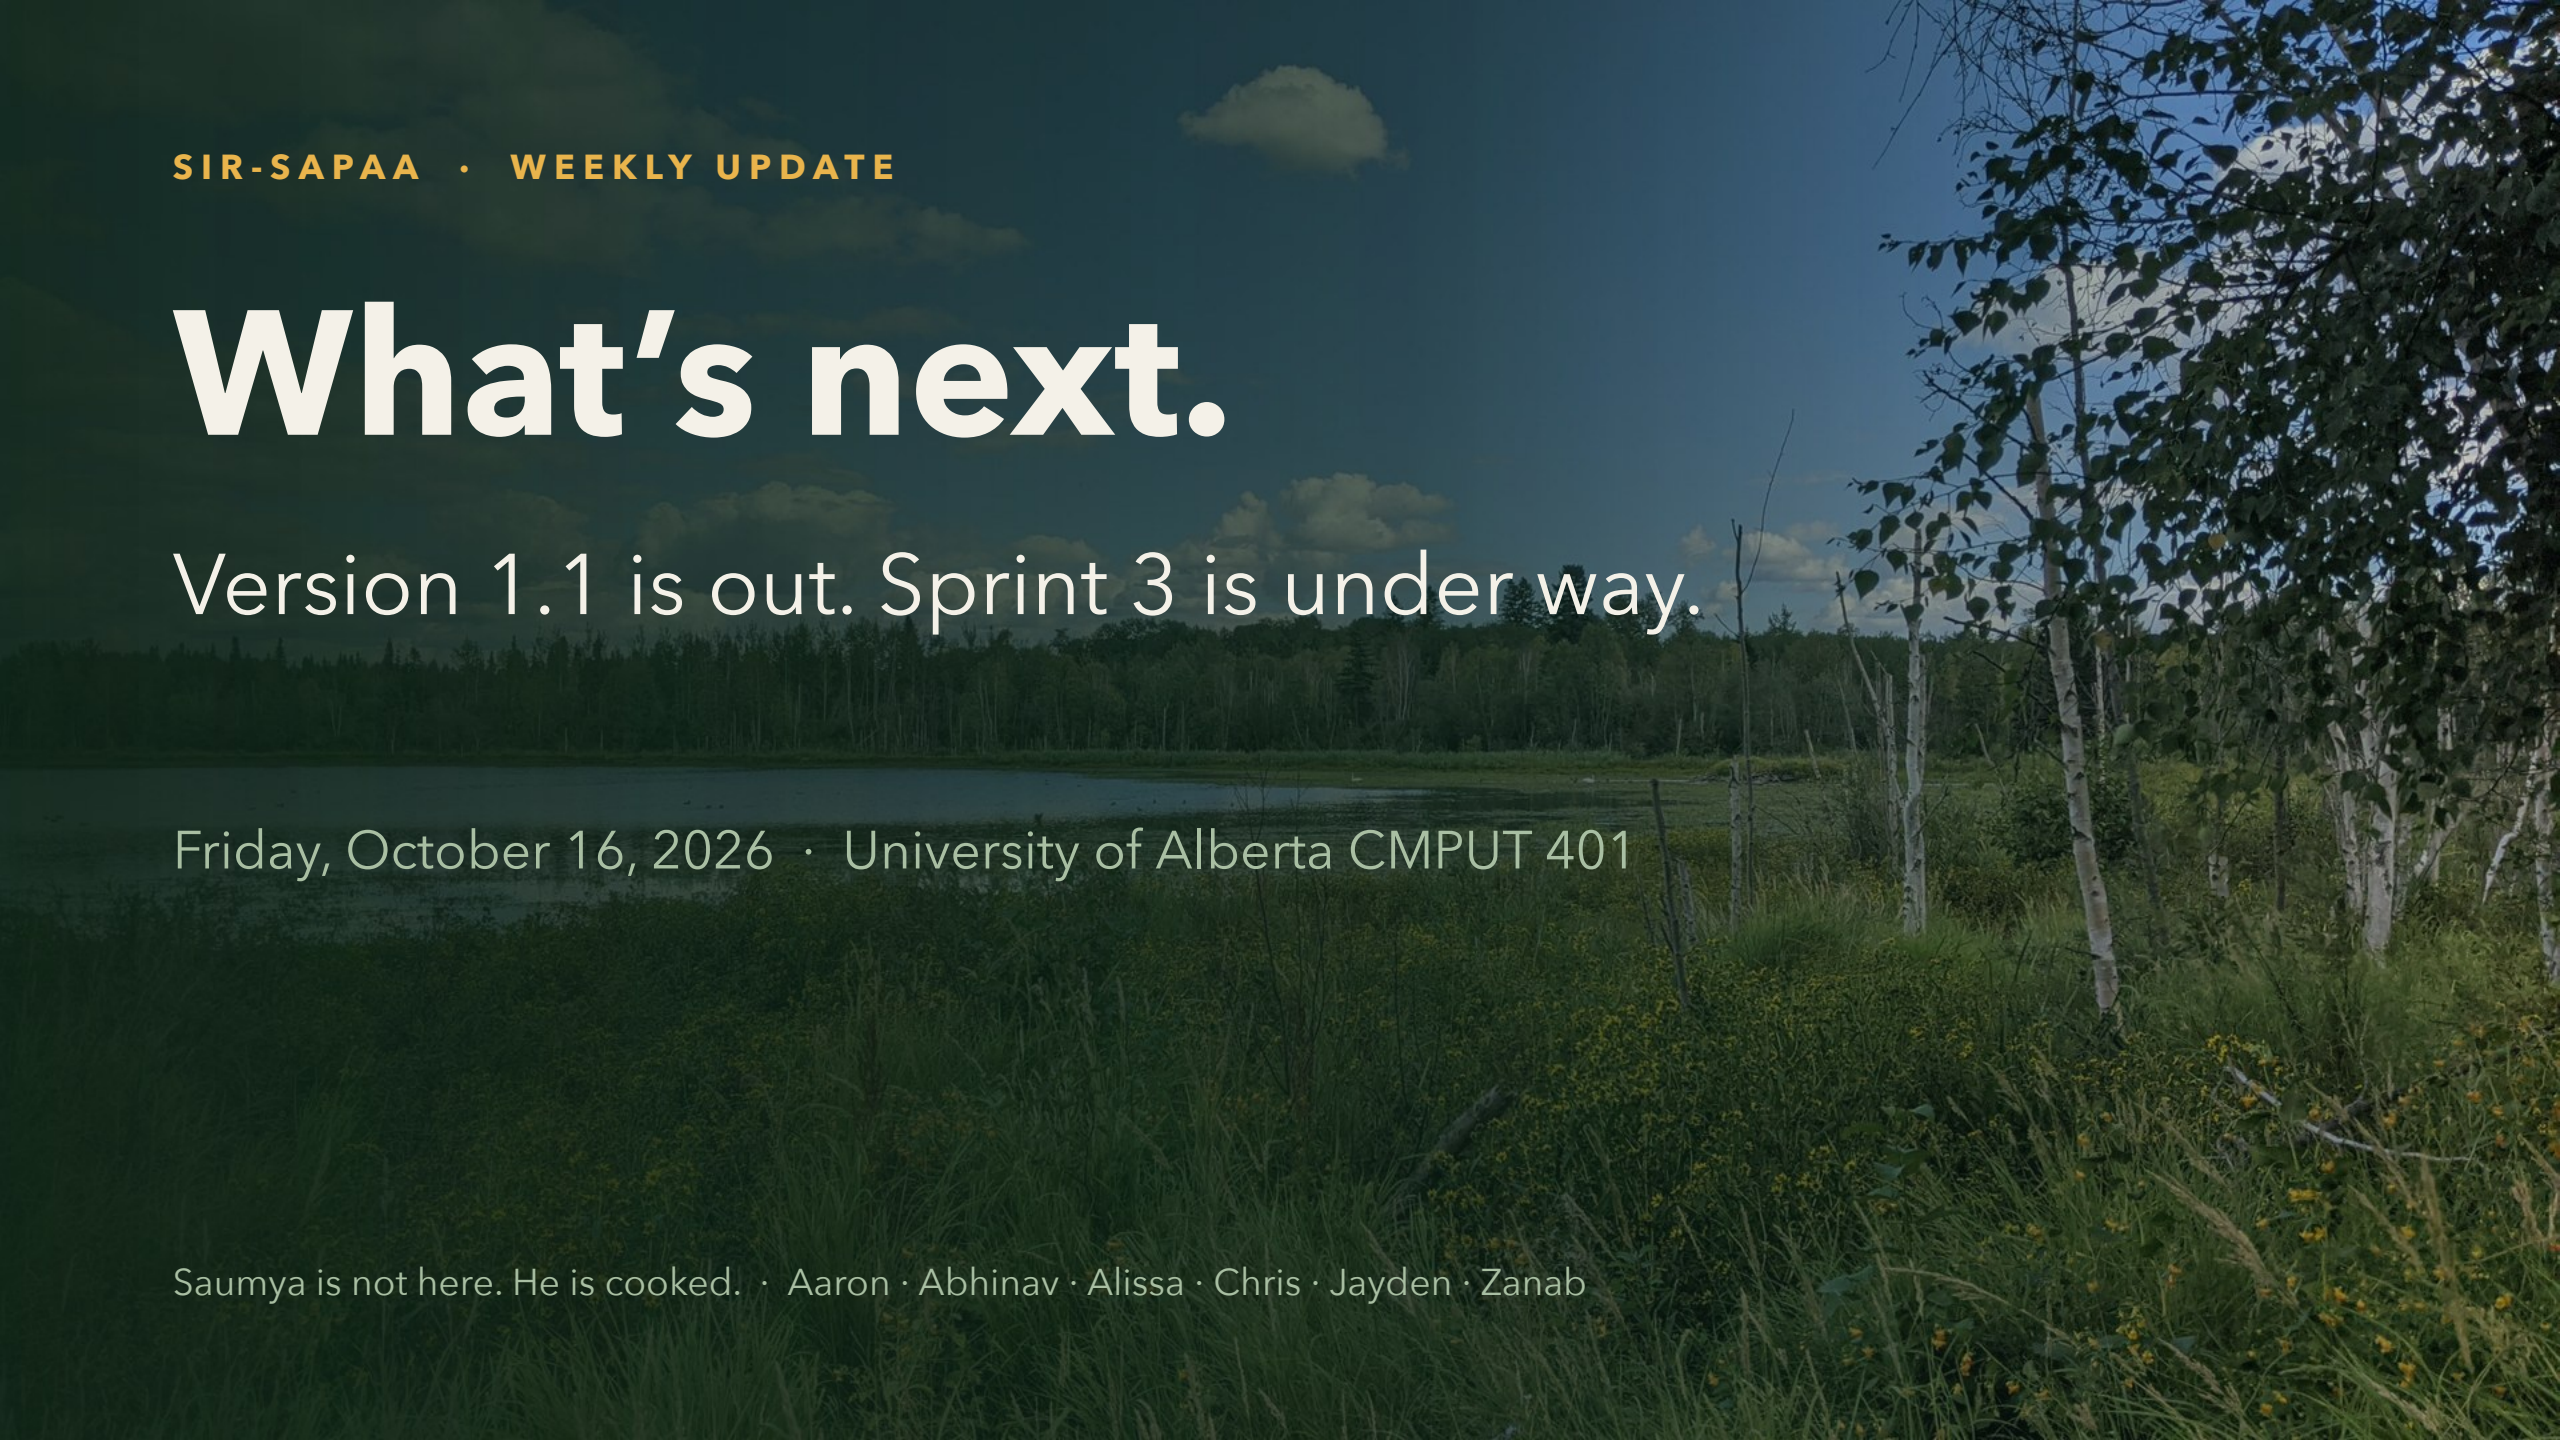


SIR-SAPAA · WEEKLY UPDATE

What's next.

Version 1.1 is out. Sprint 3 is under way.

Friday, October 16, 2026 · University of Alberta CMPUT 401

Saumya is not here. He is cooked. · Aaron · Abhinav · Alissa · Chris · Jayden · Zanab

TODAY

Three things.

1 What's new since last Friday

2 What's next: Sprint 3

3 Your version 4 email

Then what we need from you, questions from the team, and a summary.

1

What's new since last Friday

Oct 9 to Oct 16

SINCE LAST FRIDAY

Where your four projects stand.

P1	**Fixes**	Version 1.1 was released on Tuesday, Oct 13.
2a	**Testing**	Two reviewers per change. 1,524 tests passed on our machines.
2b	**People**	Profiles, history and a steward on each site all work.
2c	**Maps**	The map has boundaries, county filter and name search.

All 16 Sprint 2 stories finished: 63 of 63 points.

SINCE LAST FRIDAY

New in version 1.1.

- 2c — County, type and name filters
- 2c — Add a site from the map list
- P1 — Show or hide site page fields
- P1 — Archive, restore and delete reports
- P1 — Form keeps your place
- P1 — PDF export respects hidden fields
- 2b — Profile history, page by page
- P1 — Admin pages locked to admins

Please try it and tell us what you see.

SINCE LAST FRIDAY

What you asked us on Oct 9.

Try version 1.1	Version 1.1 is released. Please try it and tell us what you see.
Map decision	We'll write it up for your Drive, so someone can see why next year.
Sample GPX	We'll handle many files at once from the start.
Scoreboard	You added region, time period and "visited in a decade".

The scoreboard ideas are noted. Which should come first?

2

What's next

Oct 16 to Oct 23

NEXT WEEK

What we'll do, project by project.

P1	**Fixes**	Safety information on sites. Edit your past reports.
2a	**Testing**	A Sprint 3 test plan, and tests for each new story.
2b	**People**	Each past visit opens its report. Activity totals.
2c	**Maps**	Link every site to its government boundary.

OUR NEXT MEETING · FRIDAY, OCTOBER 23

What the plan has by next Friday.

Oct 16	Due today, late: boundary links · test plan · database review
Oct 17	All sites on one map · GPX storage · Safety fields · Password reset
Oct 19	“View on map” link · GPX upload checks · Activity totals
Oct 20	Safety information form · Password reset form · Past reports open
Oct 22	Site details from map · GPX tracks on map · Offline download

Planned dates. Code freeze Sunday, Oct 25. Release Tuesday, Oct 27.

SPRINT 3 · DUE TUESDAY, OCTOBER 27

Sprint 3: the map you described.

2c	**Map**	Every site and its boundary on one map. Open a site from it.
2c	**Tracks**	Upload a GPX track after a visit and see it on the map.
+	**Offline**	Download an area and keep using the map with no signal.
2b	**People**	Each past visit opens its report. Activity totals.
P1	**Reports**	Edit past reports. Safety info on sites. Password reset.

iNaturalist: public observations only, no account link. Enough?

PROJECT 2C · MAPS

The map, in your four layers.

1	**Base map**	Alberta, from OpenStreetMap data.	**Working**
2	**Boundaries**	Official area outlines.	**Drawn. Linking next.**
3	**History**	GPX tracks from stewards’ visits.	**Sprint 3**
4	**Data views**	Visit counts and scoreboard.	**Later**

We’ll build for the messy GPX files you warned us about.

THE CALENDAR WE WORK TO

Where we are on the calendar.



Sprint 1	Sprint 2	Sprint 3	Sprint 4	Sprint 5
Sep 29	**Oct 13**	**Oct 27**	**Nov 17**	**Dec 1**
Discovery and planning	Version 1.1, released	Maps and history	Room for your requests	Room for your requests

Sprints 4 and 5 may change. Your version 4 email is next.

3

Your email on version 4

Roadmap and proof of concept

YOUR EMAIL · SIR-SAPAA VERSION 4

What we read in your email and page.

Next users	Organizations that manage sites, like the Riverlot 56 Society.
Version 3	For individual volunteers, version 3 could be the last.
Versions 4 and 5	Asset tracking, site condition and volunteer activity, hopefully in 2027.
This fall	A proof of concept, field-tested in December 2026.

Source: sapaastewards.com, Oct 16, “SIR-SAPAA – Version 4, 5 & the Crown Lease”.

YOUR EMAIL · SIX REQUIREMENTS

Your six needs, and what we have.

YOUR REQUIREMENT	WHAT WE HAVE OR PLAN	WHAT IS MISSING
Legal structure	Government boundaries, sites	Who owns or leases each parcel
Tailored management	Admin can show or hide site fields	Different rules for each lease
Person management	People, roles, a steward per site	Shared roles across leases
Media, assets, GIS	Photos, map, GPX tracks (Sprint 3)	Asset records, install notes
Safety and work	Safety information on sites (Sprint 3)	Work orders, certifications
Biophysical monitoring	Inspection reports	Invasive species, fuel hazards

Our reading. We have not designed any of the missing parts yet.

OUR PROPOSAL · NOTHING DECIDED

How we’d fit it into the term.

Sprint 3	Finish the map and history. Release Oct 27.
Sprint 4	Build the proof of concept: at least two requirements.
Sprint 5	Prepare the December field test, fix what we can, hand over.
If room runs out	Activity points, visit priority, all-reports summary.

Our proposal. You decide. We’d send a short change request.

ON YOUR EMAIL

Five decisions we need from you.

1. Which two requirements for the proof of concept?
2. Who is our contact at the Riverlot 56 Society?
3. What date is the December field test, and who tests?
4. Does anything leave Sprint 4 to make room?
5. Is a short change request the right way to record it?

We’d suggest media, assets and GIS, plus person roles. They build on our map and people work.

STILL OPEN FROM EARLIER

Four things from earlier weeks.

1. Your 2021 boundary file, for go-live.
2. Your full list of site-page fields. Today we have three.
3. Harveer’s Edit Report description, or his contact.
4. Your GIS contact’s name. We’ll message them on LinkedIn.

Skip any you’ve already sent. We may have missed it.

OPEN FLOOR

Questions from the team.

Anything we need from you, based on today.

SUMMARY

Today in one slide.

This week

- Version 1.1 released Oct 13
- 63 of 63 Sprint 2 points
- County, type and name map filters
- Your version 4 email: our reading

Next week

- Link sites to boundaries
- All sites on one map
- GPX upload
- Safety info and password reset

Coming up

- Oct 27: maps and history
- Nov 17: proof of concept (proposed)
- Dec 1: final release
- December: field test



Round table.

Frank picks the order.

BACKUP · SPRINT 2

Sprint 2: final results.

STORY	PROJECT	RESULT
Steward profiles	2b	Done
Edit your own profile	2b	Done
Steward named on each site	2b	Done
Admins add a site	P1	Done, with map-list suggestions
Deactivate and reactivate a site	P1	Done
Archive, restore, delete a site	P1	Done
Edit a site	P1	Done
Links on site pages	P1	Done
Map with county filter and search	2c	Done
Photo ID optional · form keeps its page	P1	Done
Sign out from every page	P1	Done
Stewards export their own reports	P1	Done
Delete a photo	P1	Done
Hide private fields on export	P1	Done
Export more than 50 reports	P1	Done
Delete a report	P1	Done

BACKUP · SPRINT 3

Sprint 3: what you get, and when.

WHAT YOU GET	PROJECT	PLANNED
Sites linked to government boundaries	2c	Oct 16 to 19
All sites and boundaries on one map	2c	Oct 17 to 22
Open a site's details from the map	2c	Oct 21 to 22
Upload a GPX track of a visit	2c	Oct 17 to 21
Offline and online map layers	+	Oct 18 to 24
Past inspections open from profile history	2b	Oct 17 to 20
Activity totals on each profile	2b	Oct 19
Edit my previous inspections	P1	Oct 19 to 23
Safety information on each site	P1	Oct 17 to 21
Reset a forgotten password	P1	Oct 17 to 20
iNaturalist photos in the report	3a	Oct 20 to 23
Top iNaturalist observations on a site	3a	Oct 21 to 23

Freeze Sunday, Oct 25. Release Tuesday, Oct 27. "+" = team request, not in your charter. 3a = iNaturalist.
