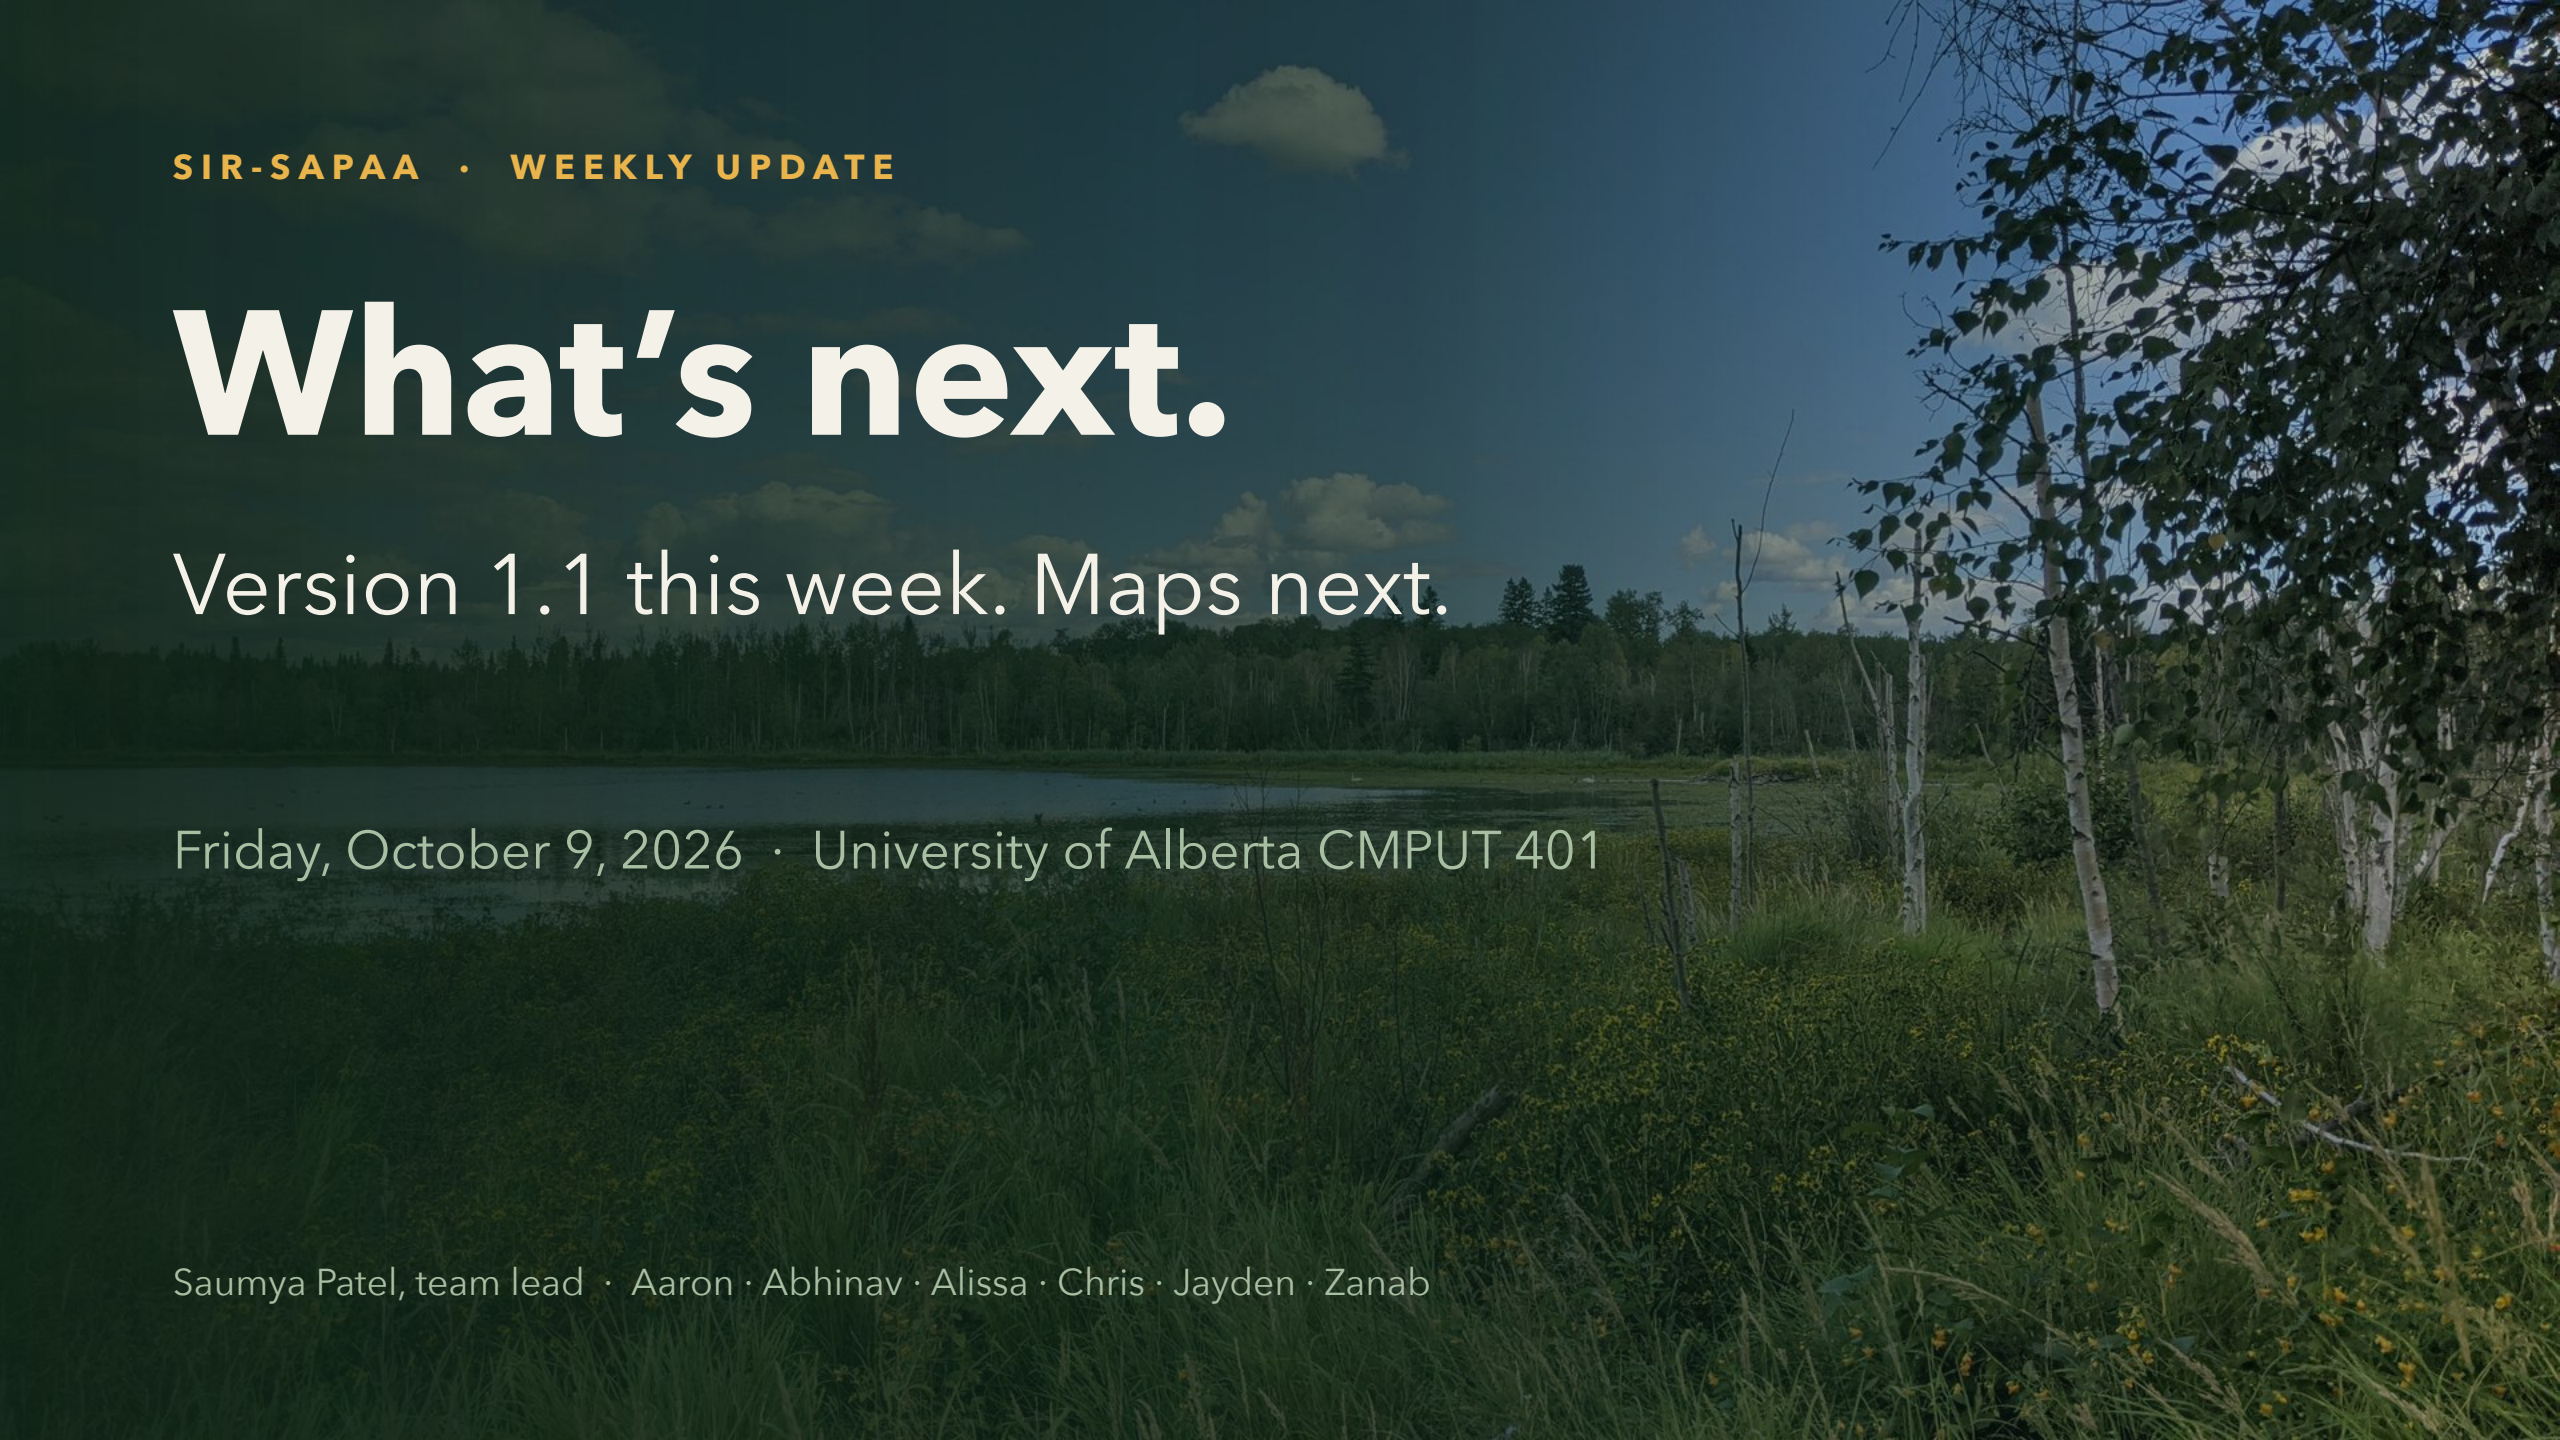


SIR-SAPAA · WEEKLY UPDATE

What's next.

Version 1.1 this week. Maps next.

Friday, October 9, 2026 · University of Alberta CMPUT 401

Saumya Patel, team lead · Aaron · Abhinav · Alissa · Chris · Jayden · Zanab

TODAY

Three things.

1 What's new since last Friday

2 Your asks from last Friday

3 What's next

Then what we need from you, questions from the team, and a summary.

1

What's new since last Friday

Oct 2 to Oct 9

SINCE LAST FRIDAY

Where your four projects stand.

P1	**Fixes**	Version 1.1 is nearly built. Five pieces are in review.
2a	**Testing**	Two teammates review every change before it goes in.
2b	**People**	Steward profiles work, with a steward named on each site.
2c	**Maps**	The map shows Alberta and government protected-area boundaries.

About 30 code changes merged since last Friday, including 6 fixes.

SINCE LAST FRIDAY

Ready to see in the practice copy.

- 2c — Map view with protected-area boundaries
- 2b — Steward named on each site page
- P1 — Archive, restore or delete a site
- P1 — Download your own report as a PDF
- 2b — Steward profile with inspection history
- P1 — Admins add a site
- P1 — Sign out from every page
- P1 — Hide private fields before export

Want to see any of these now? We can demo it.

2

Your asks from last Friday

Map, releases, scoreboard, deleting

YOUR ASK · PROJECT 2C · MAPS

Which map, and why.

Our choice	OpenStreetMap data, shown with Protomaps and MapLibre.
Not Google	Google’s terms don’t permit offline use of its maps in another app.
Already working	It runs in the app today, with government boundaries on it.
Still to confirm	Hosting cost, non-profit terms and offline saving.

How often you get new versions.

Every sprint	A new version at the end of each sprint: Oct 13, Oct 27, Nov 17, Dec 1.
You see it first	We demo each release to you until you trust our testing.
Checked first	Two teammates review each change and automatic checks run before release.
Frozen early	No new work in the last two days, so only tested work ships.

No single big release at the end of term. Does this work for you?

YOUR ASK · PROJECT 2B · MOCKUP

A simple scoreboard: our mockup.

42
inspections

Top contributor
Most inspections submitted.

9
counties

County explorer
Most different counties visited.

17
sites

Site variety
Most different sites inspected.

5
sites

First on site
First report ever filed at a site.

Example numbers, not real data. The counts use data we already store.

YOUR ANSWER · PROJECT 1 · DELETING

Deleting, in two safe steps.

Archive	Hides a site. Nothing is lost. An admin can restore it.
Delete for good	Removes the site and its steward link. Reports and photos stay.
Reports	Reports get the same two steps. In review now.
Your call	Do you want a milder level below archive, “suppress”?

3

What's next

Oct 9 to Oct 16

NEXT WEEK

What we'll do, project by project.

P1	**Fixes**	Finish version 1.1 and release it on Tuesday, Oct 13.
2a	**Testing**	Release through the new review process.
2b	**People**	Each past visit opens its report. Scoreboard totals next.
2c	**Maps**	Link sites to their government boundaries.

OUR NEXT MEETING · FRIDAY, OCTOBER 16

What you can expect next Friday.

Oct 11	Version 1.1 frozen: all of it merged and tested
Oct 12	Release notes written
Oct 13	Version 1.1 released to stewards
Oct 14	Team demo and review · Sprint 3 planned
Oct 16	Sites linked to their boundaries · Sprint 3 test plan · database review

The live database needs a one-time update at release, with your admin, so Supaview can connect.

VERSION 1.1 · STILL IN REVIEW

Five last pieces of version 1.1.

P1	**Add site**	Warns about similar site names.
P1	**Edit site**	Admins choose which site fields to show, hide and edit.
P1	**Your form**	The form reopens on the page you left.
P1	**Reports**	Admins archive or permanently delete a report.
2c	**Map**	Filter the map by type, and search by name.

Your form problem is nearly fixed.

Before	At River Lot 56 we left the app mid-form. It reopened on page one. Answers were saved, but we clicked forward again.
Now	The form reopens on the page you left, with your answers.
When	In review today. We aimed for Oct 6. Now: version 1.1 on Oct 13.

SPRINT 3 · DUE TUESDAY, OCTOBER 27

Sprint 3: the map you described.

2c	**Map**	Every site and its boundary on one map. Open a site from it.
2c	**Tracks**	Upload a GPX track after a visit and see it on the map.
+	**Offline**	Download an area and keep using the map with no signal.
2b	**People**	Open any past visit from a profile. Scoreboard totals.
P1	**Reports**	Edit past reports. Safety info on sites. Password reset.

iNaturalist import is planned too. Tell us if you'd rather defer it.

PROJECT 2C · MAPS

The map, in your four layers.

1	**Base map**	Alberta, from OpenStreetMap data.	**Working**
2	**Boundaries**	Government protected-area polygons.	**On the map. Linked to sites by Oct 16.**
3	**History**	GPX tracks from stewards' visits.	**Sprint 3**
4	**Data views**	Visit counts and scoreboard on the map.	**Later**

2023 data is fine for testing. For go-live we need your 2021 file.

THE CALENDAR WE WORK TO

Where we are on the calendar.



Sprint 1

Sept 29

Discovery and planning

Sprint 2

Oct 13

Version 1.1

Sprint 3

Oct 27

Maps and history

Sprint 4

Nov 17

Room for your requests

Sprint 5

Dec 1

Room for your requests

Sprint 2 ends Tuesday. Sprint 3 starts the next day.

SPRINTS 4 AND 5 · NOV 17 AND DEC 1

Sprints 4 and 5 are still yours.

Sprint 4 · Nov 17

- **Your new requests**
- Activity points for stewards
- Which sites most need a visit
- Download all photos and files
- Summary charts across all reports

Sprint 5 · Dec 1

- **Your new requests**
- Fixes from the December field test
- Final polish and handover notes

You said you'd flesh out version 3.0 in October. We'd love to see it.

WHAT WE NEED FROM YOU

Five things we need from you.

1. Your 2021 boundary file, for go-live.
2. Your full list of site-page fields. Today we have three.
3. Harveer’s Edit Report description, or his contact.
4. Your GIS contact. We’ll reach out on LinkedIn.
5. iNaturalist import: this term, or defer?

And your answers on the map, releases and deleting.

OPEN FLOOR

Questions from the team.

Anything we need from you, based on today.

SUMMARY

Today in one slide.

This week

- About 30 code changes merged
- Version 1.1 nearly built
- Protected-area boundaries on the map
- Steward on each site

Next week

- Release version 1.1
- Sites linked to boundaries
- Scoreboard on profiles
- Your decisions

Coming up

- Oct 27: maps and history
- Nov 17 and Dec 1: your requests
- December: field test



Round table.

Frank picks the order.

BACKUP · SPRINT 2

Sprint 2: where each story stands.

STORY	PROJECT	STATUS AS OF OCT 9
Steward profiles	2b	Merged
Edit your own profile	2b	Merged
Steward named on each site	2b	Merged
Admins add a site	P1	Merged. Name warning in review. Boundary picking not built
Deactivate and reactivate a site	P1	Merged
Archive, restore, delete a site	P1	Merged
Edit a site	P1	In review
Links on site pages	P1	Merged
Map with county filter and search	2c	Boundaries merged. Type filter in review. No county filter yet
Photo ID optional · form keeps its page	P1	Photo ID merged. Form fix in review
Sign out from every page	P1	Merged
Stewards export their own reports	P1	Merged
Delete a photo	P1	Merged
Hide private fields on export	P1	Merged
Export more than 50 reports	P1	Being verified
Delete a report	P1	In review

BACKUP · SPRINT 3

Sprint 3: what you get, and when.

WHAT YOU GET	PROJECT	BUILT
Sites linked to government boundaries	2c	Oct 16 to 19
All sites and boundaries on one map	2c	Oct 17 to 22
Open a site’s details from the map	2c	Oct 21 to 22
Upload a GPX track of a visit	2c	Oct 17 to 21
Offline and online map layers	+	Oct 18 to 24
Past inspections open from profile history	2b	Oct 17 to 20
Activity totals on each profile	2b	Oct 19
Edit my previous inspections	P1	Oct 19 to 23
Safety information on each site	P1	Oct 17 to 21
Reset a forgotten password	P1	Oct 17 to 20
Connect iNaturalist and pick photos	3a	Oct 20 to 23
Top iNaturalist observations on a site	3a	Oct 21 to 23

Freeze Sunday, Oct 25. Release Tuesday, Oct 27. “+” = team request, not in your charter. iNaturalist rows can be deferred.
